


ID	Task Mode	Task Name	Duration	Start	Finish	Qtr 1, 2022		Qtr 2, 2022		Qtr 3, 2022		Qtr 4, 2022		Qtr 1, 2023		Qtr 2, 2023
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov
1	➡	<b>Off-site Pump Station &amp; Force Main</b>	<b>101 days</b>	<b>Fri 6/3/22</b>	<b>Fri 10/21/22</b>											
2	➡	<b>Force Main</b>	<b>101 days</b>	<b>Fri 6/3/22</b>	<b>Fri 10/21/22</b>											
3	➡	Mill Section A	1 day	Fri 6/3/22	Mon 6/6/22											
4	📅	4" Force Main - Section A	20 days	Mon 6/6/22	Fri 7/1/22											
5	➡	Asphalt Patching - Section A	2 days	Mon 7/4/22	Tue 7/5/22											
6	➡	Mill Section B	1 day	Fri 7/1/22	Mon 7/4/22											
7	➡	4" Force Main - Section B	12 days	Mon 7/4/22	Tue 7/19/22											
8	➡	Asphalt Patching - Section B	1 day	Wed 7/20/22	Wed 7/20/22											
9	➡	Mill Section C	1 day	Tue 7/19/22	Wed 7/20/22											
10	➡	4" Force Main - Section C	12 days	Wed 7/20/22	Thu 8/4/22											
11	➡	Asphalt Patching - Section C	1 day	Fri 8/5/22	Fri 8/5/22											
12	➡	Mill Section D	1 day	Thu 8/4/22	Fri 8/5/22											
13	➡	4" Force Main - Section D	11 days	Fri 8/5/22	Fri 8/19/22											
14	➡	Asphalt Patching - Section D	1 day	Mon 8/22/22	Mon 8/22/22											
15	➡	Vacuum Testing	4 days	Tue 8/23/22	Fri 8/26/22											
16	➡	Wearing Paving - Section A through D	2 days	Thu 10/20/22	Fri 10/21/22											
17	➡	<b>Pump Station</b>	<b>50 days</b>	<b>Mon 6/6/22</b>	<b>Fri 8/12/22</b>											
18	📅	Grade Pump Station Pad	5 days	Mon 6/6/22	Mon 6/13/22											
19	➡	Excavate Wet Well	2 days	Mon 6/13/22	Wed 6/15/22											
20	📅	Deliver, Install & Backfill Wet Well	4 days	Wed 6/15/22	Mon 6/20/22											
21	➡	8" Gravity Sewer to 3" FM	3 days	Tue 6/21/22	Thu 6/23/22											
22	➡	Vacuum Testing	2 days	Fri 6/24/22	Mon 6/27/22											
23	➡	Electrical Equipment Backboard & Controls	10 days	Tue 6/28/22	Mon 7/11/22											
24	➡	Generator Distribution and Concrete Pad	5 days	Tue 7/12/22	Mon 7/18/22											
25	➡	Electrical Distribution Installation	5 days	Tue 7/19/22	Mon 7/25/22											
26	➡	Asphalt Paving	3 days	Tue 7/26/22	Thu 7/28/22											
27	➡	Re-spread Topsoil	2 days	Fri 7/29/22	Mon 8/1/22											
28	➡	Install Fence & Gates	4 days	Tue 8/2/22	Fri 8/5/22											
29	➡	Start-up & Closeout	3 days	Wed 8/10/22	Fri 8/12/22											
30	📅	Generator Lead Time	310 days	Tue 2/1/22	Mon 4/10/23											
31	📅	Install Generator & Misc. Controls	5 days	Tue 4/11/23	Mon 4/17/23											
32	➡															
33	➡															
34	➡															
35	➡															
36	➡															
37	➡															
38	➡															

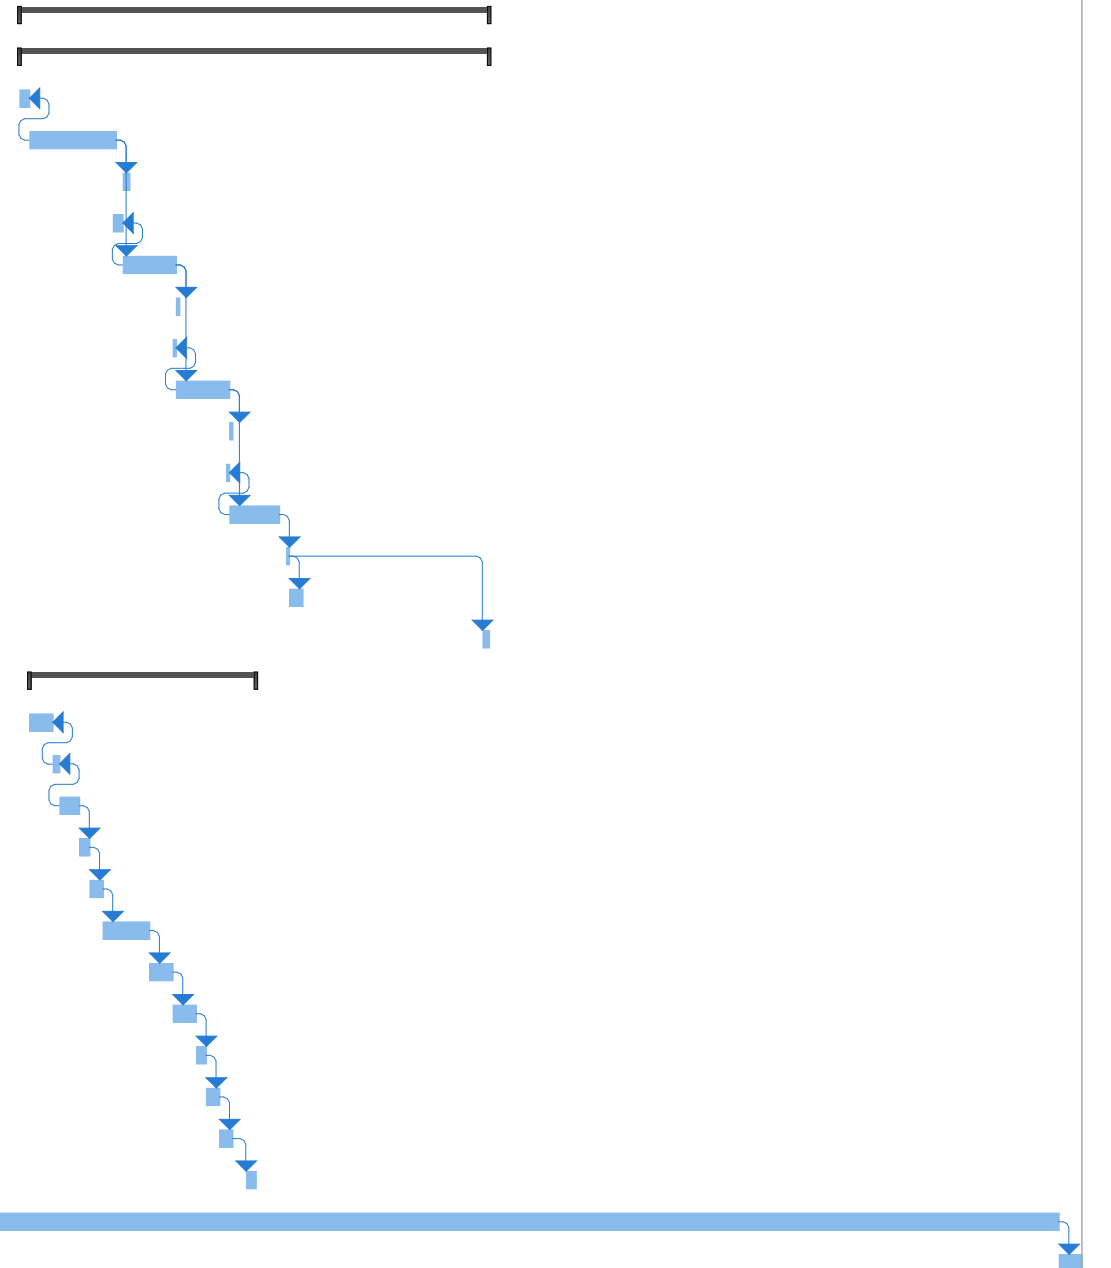

Project: Pump Station & FM Sch  
Date: Wed 5/25/22

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

**Section A (STA 0+00 to 13+00) – 1,300 LF**

Day 1 – Hillwood Frontage (1+60)

Day 2 – Hillwood Frontage (2+80)

Day 3 – Hillwood Frontage (4+00)

Day 4 – Hillwood Frontage (5+20)

Day 5 – Hillwood Frontage (6+40)

Day 6-15 – Pump Station & Gravity Sewer

Day 16 – Hillwood Frontage (7+60)

Day 17 – Hillwood Frontage (8+80)

Day 18 – Hillwood Frontage (10+00)

Day 19 – Hillwood Frontage (11+20)

Day 20 – Hillwood Frontage (12+80)

**Section B (STA 13+00 to 27+00) – 1,400 LF**

Day 21 – Hillwood Frontage (14+20)

Day 22 – 1060 Canal Rd: Martin Residence (15+40)

Day 23 – 1070 Canal Rd: Naylor Residence (16+60)

Day 24 – 1090 Canal Rd: Humbert Residence (17+80)

Day 25 – 1090 Canal Rd: Humbert Residence (19+00)

Day 26 – 1090 Canal Rd: Humbert Residence (20+20)

Day 27 – 1130 Canal Rd: Maldonado Residence (21+25)

Day 28 – 1130 Canal Rd: Maldonado Residence (21+70)

Day 29 – 1130 Canal Rd: Maldonado Residence (22+90)

Day 30 – 1160 Canal Rd: Koons Residence (24+50)

Day 31 – 1160 Canal Rd: Koons Residence (25+70)

Day 32 – 1180 Canal Rd: Shelley Residence (27+00)

**Section C (STA 27+00 to 41+00) – 1,400 LF**

Day 33 – Gross Frontage (28+60)

Day 34 – Gross Frontage (30+00)

Day 35 – Gross Frontage (31+40)

Day 36 – Gross Frontage (32+80)

Day 37 – Gross Frontage (34+00)

Day 38 – Gross Frontage (34+00)

Day 39 – Gross Frontage (35+40)

Day 40 – Gross Frontage (36+60)

Day 41 – Gross Frontage (37+80)

Day 42 – Gross Frontage (39+00)

Day 43 – Gross Frontage (40+20)

Day 44 – Gross Frontage (41+00)

**Section D (STA 41+00 to 54+64) – 1,364 LF**

Day 45 – Gross Frontage (43+00)

Day 46 – Gross Frontage (44+40)

Day 47 – Gross Frontage (45+80)

Day 48 – Manchester St Intersection (46+60)

Day 49 – 315 Manchester St: McMaster Residence (47+80)

Day 50 – 285 Manchester St: Irvin Residence (49+00)

Day 51 – 285 Manchester St: Irvin Residence (50+20)

Day 52 – 275 Manchester St: Zeigler Residence (51+40)

Day 53 – 255 Manchester St: Lynam Residence (52+80)

Day 54 – 245 Manchester St: Rodgers Residence (54+20)

Day 55 – Tie-In to EX MH 35 (54+64)

Day 56 – Asphalt Patching of Section D

Day 57 – Testing

Day 58 – Testing

Day 59 – Testing

Day 60 – Testing

\*Kinsley will follow up with timeframe of Final Wearing Paving
